

The M.U.D. Report (Monday Updates & Developments)

OBP Crew

Location: Franconia/Old Bridal Path

Dates:

5/27/24 - 5/30/24

6/3/24 - 6/6/24

Project Summary & Goals:

Rock stairs, two reroutes around highly impacted sections. Cairns and scree wall above tree line.

The Crew:

Lou Kimball (Crew Lead)
Tobin Vignos
Tahlia Torres-Cohen
Izzy Hughes
Julia Goode

By The Numbers (#s from work report)

Total Crew Hours	350	Obscuring/Naturalizing	35 Square Feet
Rock Steps	21, Average 3FT Width	Corridor Clearing/Standardizing	300 Linear Feet
Gargoyles/Set Scree	33	Drainage Ditch Cleaned	23
Rock Water Bar	2 totaling 19 Linear Feet	Rock Hardened Drain	12 sq ft
Crush Made	37 Cubic Feet	Scree Wall	32 Cubic Feet

Partner Crews:

-OBP Trailworks LLC

Total Hours: 140

-Old Soul Stone Works LLC

Total Hours: 60

Successes:

The project is off and running, picking up right where we left off last fall. With many folks on the crew having less experience with masonry, we have focused the first couple weeks on cycling people through all sorts of tasks. People are taking to the drilling and splitting with ease and we have been able to make enough material to open up multiple sites and put in 21 new steps.



Before



After

Challenges:


Much of our material is at this point below the current work site, so the crew has been hand carrying rock with a rock litter up to the site.

Shoutout:

This week Tobin and Izzy took a large boulder and split it into 12 beautiful step pieces




Before

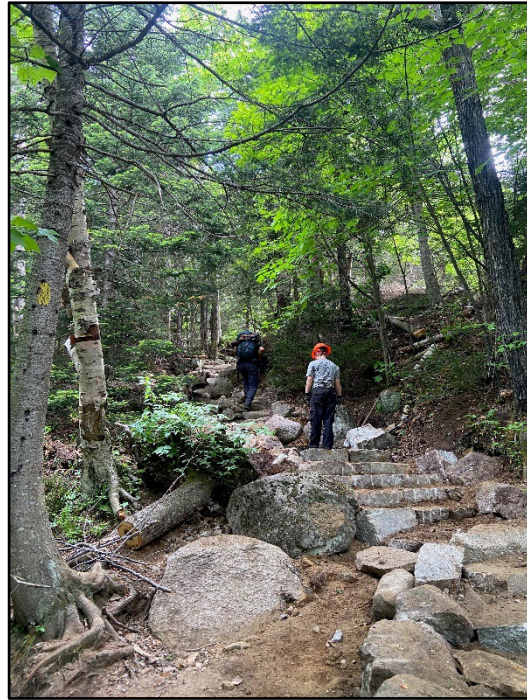

After

Action Shots:

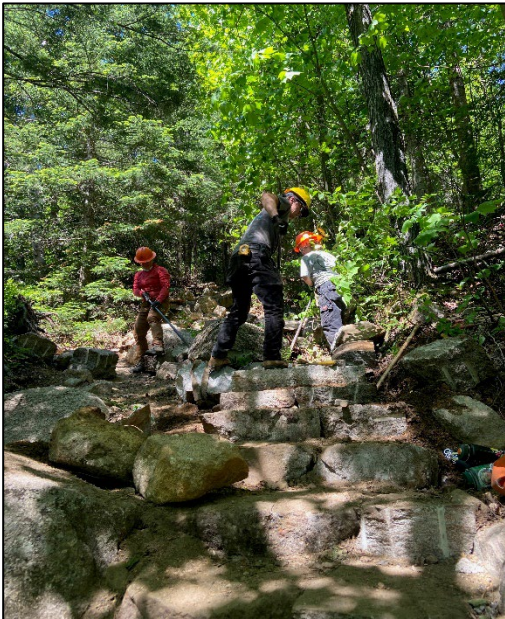

Jordan, Deva and Julia moving rocks



Izzy Digging
